## Carlsbad Boulevard Realignment Program Status Report





## Today's Presentation

- Review current conditions
- Review past city direction
- What has been completed
- What is underway
- What is plan for the future














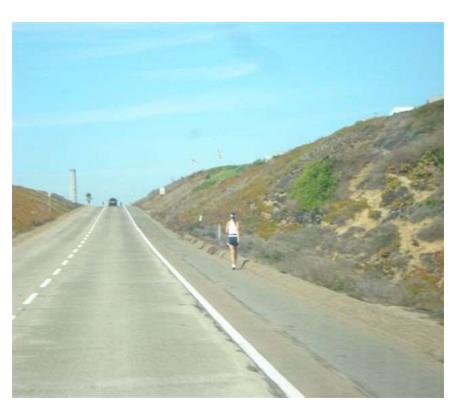





















#### Past Direction

October 2013 Council direction

"Pursue livable streets improvements within the Carlsbad Boulevard right-of-way, with an expanded south to north boundary."





#### Past Direction

- Carlsbad Community Vision
- "World Class City"
- 2014 Carlsbad Resident Survey
  - Four Focus Groups
- 2015 City Council goal setting



## Recently Completed Projects

- CVD & Grand Pedestrian Scrambles
- Carlsbad Boulevard Crosswalks
- Carlsbad Boulevard Lane Stripping/Overlay
- State Street Roundabout
- "Carlsbad" Sign



#### CVD & Grand Pedestrian Scrambles







#### Carlsbad Boulevard Crosswalks







#### Carlsbad Boulevard Crosswalks





## Carlsbad Boulevard Lane Stripping/Overlay





























## "Carlsbad" Sign





## Work Underway

- Carlsbad Boulevard Railroad Bridge
- Coastal Corridor Multi-Modal Infrastructure Plan



## Carlsbad Boulevard Railroad Bridge

- Bridge rail replacement, sidewalk improvements, lane narrowing
- Construction started January 2015
- Construction Completed by June 2015
- \$1,269,300 project



## Coastal Corridor Multi-Modal Infrastructure Plan

- Roadmap to activate the goals and policies of the new GP Mobility Element
- Identify ways to link users to activity centers along the Carlsbad coastline
- Initiated December 2014
- Complete in November 2015
- \$100,000 project budget



## Planned Projects

- Tamarack Ave/Carlsbad Blvd Intersection Pedestrian Improvements
- Carlsbad Blvd Improvements Cannon Rd to Manzano Dr
- South Carlsbad Blvd Manzano Dr to southern city limit






















- Outreach, design, permitting; Mar-Nov 2015
- Construction drawings, bid prep, selection, and award contract; Dec 2015 – Aug 2016
- Start and Complete Construction; Sept 2016
   Jan 2017
- \$455K in FY 14/15 CIP funding; Seeking
  \$270K in SANDAG Grant; \$725K total







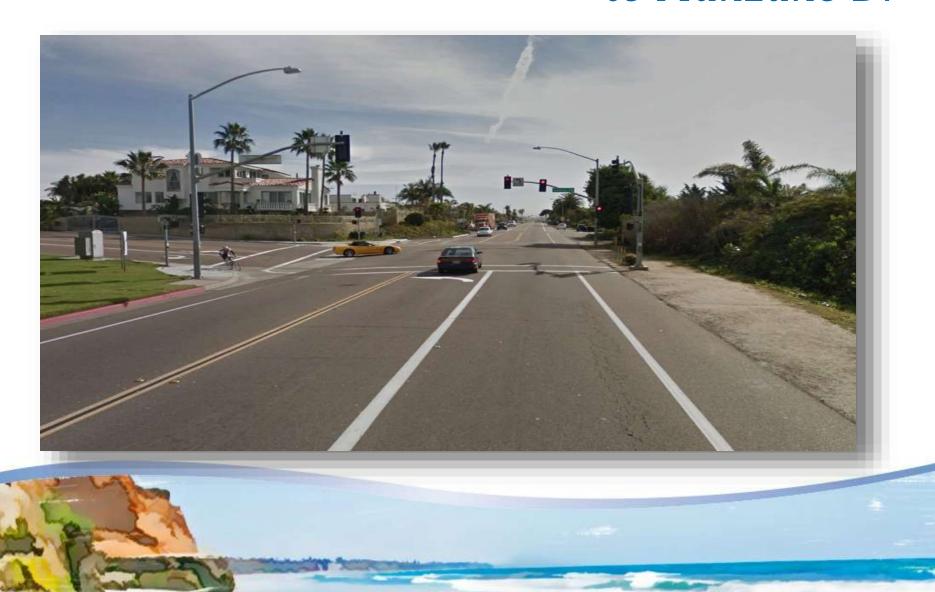












- Outreach, design, permitting; Mar-Dec 2015
- Construction drawings, bid prep, selection,
  and award contract; Jan Aug 2016
- Start and Complete Construction; Sept 2016
   Jun 2017
- \$6 mill in FY 14/15 CIP funding



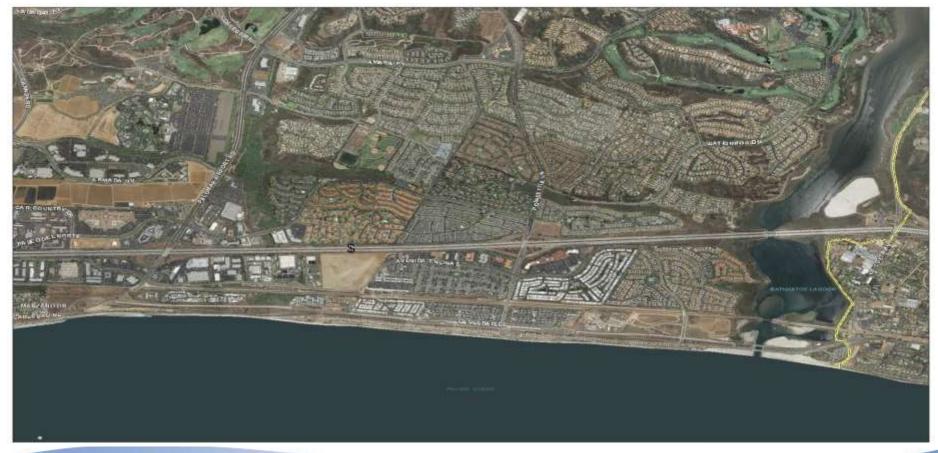










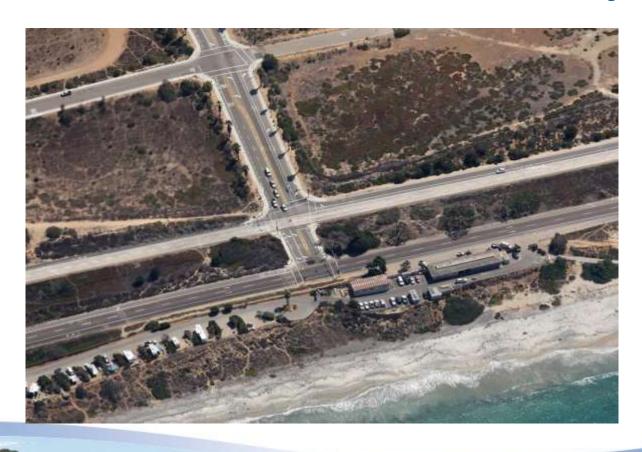















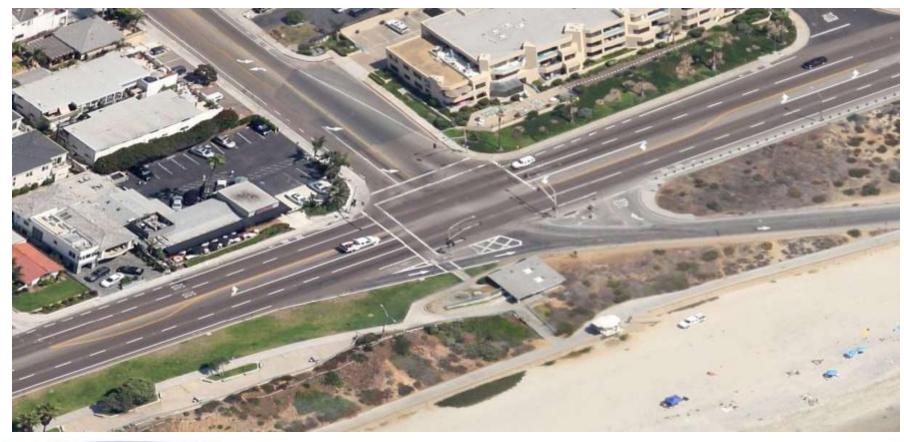







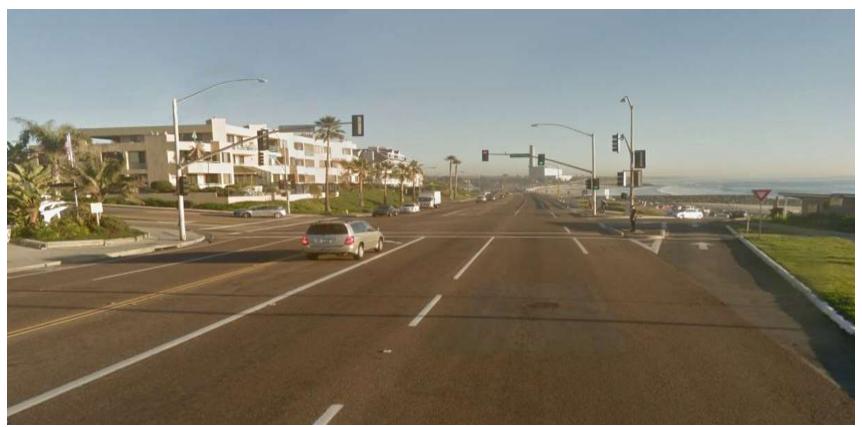












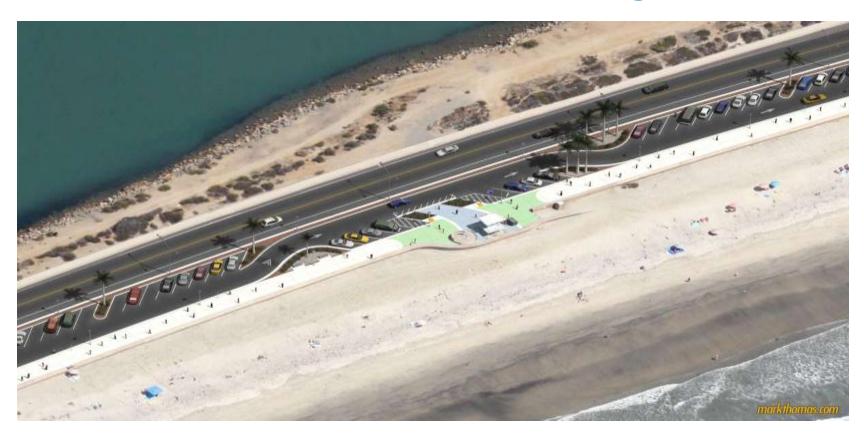




























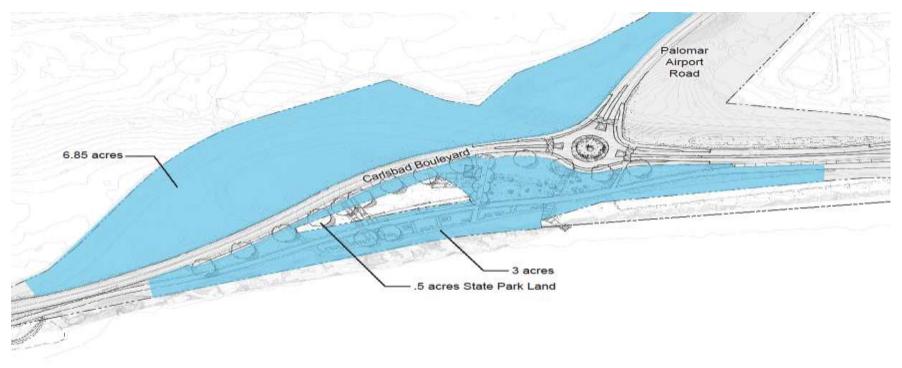


CARLSBAD BOULEVARD: Alternative 2 - Area Calculations n.t.s. 2014-02-21

A=COM



## Looking Forward

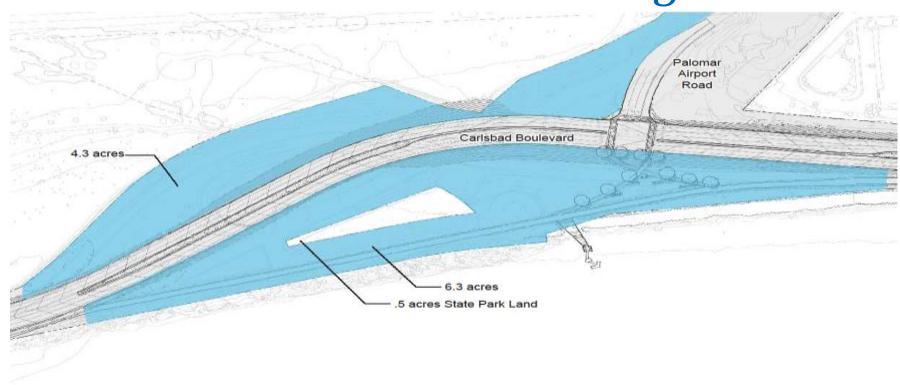


CARLSBAD BOULEVARD: Alternative 1 - Area Calculations n.t.s. 2014-02-21





## Looking Forward

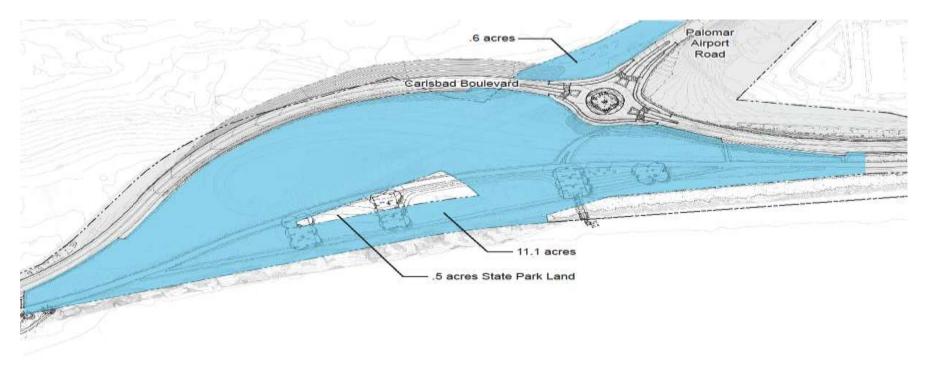

CARLSBAD BOULEVARD: Alternative 3 - Area Calculations n.t.s. 2014-02-21









## Carlsbad Boulevard Realignment Program Status Report

# Questions?

